

Proposed Implementation Timeline

Online Job Offer System | One Full-Stack Developer | Baseline: 30 Weeks

Version 1.0 • 21 July 2026

Executive Summary


A practical baseline is 30 calendar weeks from approved kickoff to production handover for one dedicated full-stack developer. The plan sequences the highest-risk foundations first—data model, access control, salary rules, proposal versioning, and approval routing—then completes candidate outcomes, documents, reporting, integration testing, UAT, and deployment.

Planning Item	Proposed Position
Recommended baseline	30 weeks
Target MVP feature-complete	End of Week 23
System/UAT stabilization	Weeks 24-28
Production release	Week 30
Delivery capacity assumption	1 developer, ~80% planned delivery capacity
Estimate confidence	Planning estimate; refine after discovery and technical platform confirmation

Scope Basis

The estimate covers the end-to-end workflow described in the supplied sources: candidate intake through MS Forms, validation, legal-entity salary matrix selection, one-to-three proposal options, salary-band calculations, per-option approval decisions, President escalation for above-band offers, reminders/escalations, candidate discussion and re-proposal, offer-letter generation, delegation, audit history, governance reporting, and role-based access.

Delivery Timeline at a Glance

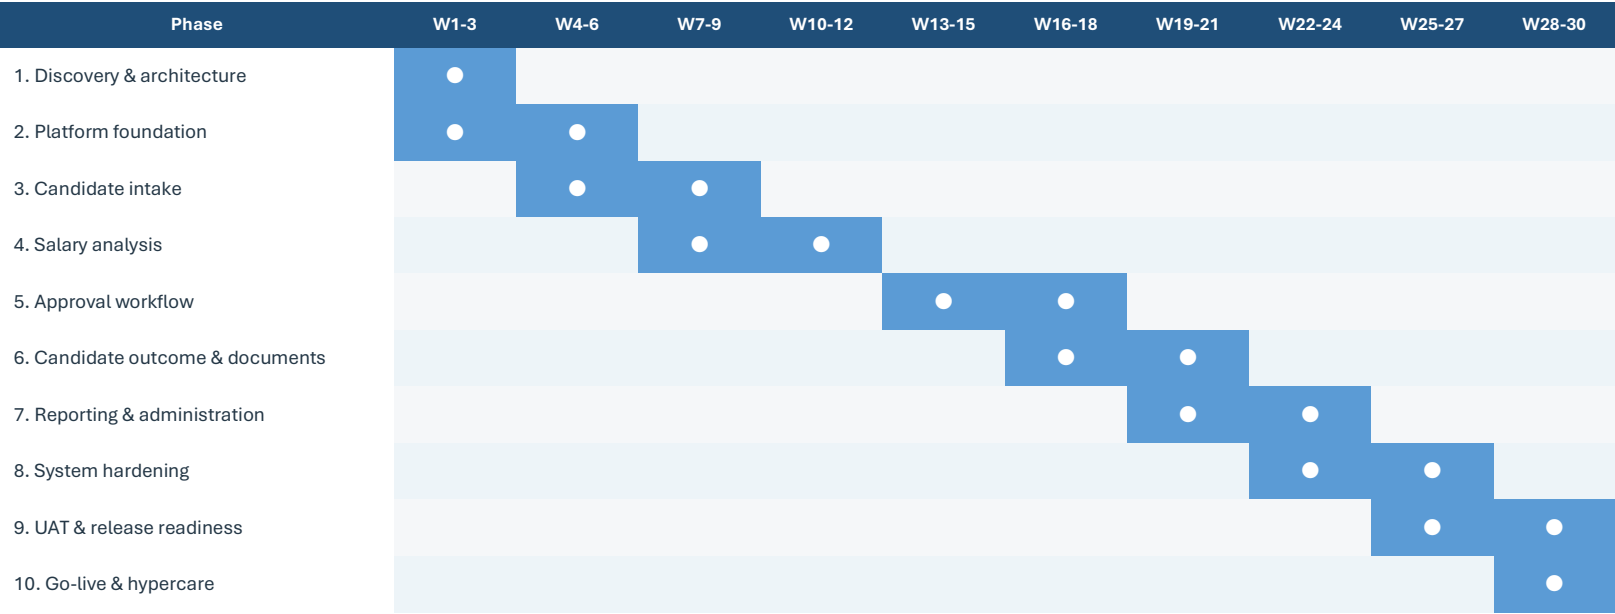

Detailed Phase Plan

#	Weeks	Workstream	Key Activities	Exit Deliverable	Scope Trace
1	W1-2	Discovery & solution architecture	Confirm platform, integrations, non-functional needs, workflow states, roles, data model, environments, backlog and acceptance approach.	Approved solution outline; prioritized backlog; architecture/data model; delivery setup	All; BL-01 to BL-20
2	W3-5	Foundation, security & master data	Project skeleton, database migrations, authentication, RBAC/ABAC, legal entities, requisitions, users, approver matrix, salary-matrix administration and audit framework.	Working secured application; core master-data screens/APIs; CI/CD baseline	US-04, US-16, US-19; BL-01, 04-05, 17-18
3	W6-8	Candidate intake & validation	Create job-offer case, MS Forms handoff/import approach, file validation/storage, submission tracking, correction loop and TA validation.	Traceable candidate intake; validated package workflow	US-01 to US-03
4	W9-12	Salary analysis & proposal engine	Effective-dated matrix lookup; 1-3 proposal options; compa-ratio, increase and band-position calculations; exception flags; proposal version model.	Job Offer Analysis with reliable calculations and validation	US-04 to US-06, US-13, US-19; BL-05 to 09
5	W13-17	Approval routing & notifications	Per-option decisions, HROD/Division approval, President escalation, rejection comments, secure task links, email/in-app notices, reminders, escalation, retries and delivery logs.	End-to-end approval workflow with SLA handling	US-07 to US-11, US-20, US-21; BL-10 to 12, 19
6	W18-20	Candidate decision, re-proposal & offer letter	Approved-options-only discussion, accept/decline/negotiation, new proposal cycles with history, final offer merge and secure document storage.	Candidate outcome workflow; generated offer letter	US-12, US-13, US-15; BL-13 to 16
7	W21-23	Delegation, dashboards & governance	Delegate/reassign/shadow access, transaction history, HRBP status view, above-band report, filters/export and administration refinements.	Feature-complete MVP; operational dashboards and reports	US-14, US-16 to US-18; BL-17, 18, 20
8	W24-26	Integration, security & system testing	End-to-end scenarios, negative paths, authorization checks, audit reconciliation, file security, notification failures, performance checks, backups and defect repair.	Release candidate; system test evidence; operating notes	All stories and business rules
9	W27-29	UAT, remediation & release readiness	Business-led UAT, developer fixes, regression, data/config preparation, user/admin guidance, deployment rehearsal and go-live approval.	UAT sign-off; deployment package; support runbook	All acceptance criteria
10	W30	Production deployment & hypercare	Production release, smoke tests, monitoring, priority defect response, handover and backlog closure review.	Live system; handover; post-launch backlog	All

Milestones and Decision Gates

Gate	Target	Milestone	Exit Criteria
M1	End W2	Scope and architecture approved	Platform/integration decisions and backlog are sufficiently clear to build.
M2	End W8	Intake workflow demo	TA can create a case, receive/validate candidate inputs, and see an auditable status history.
M3	End W12	Salary engine demo	Matrix lookup, calculations, band flags, and proposal versioning pass agreed examples.
M4	End W17	Approval workflow demo	Normal and above-band paths, per-option decisions, reminders, and escalation work end to end.
M5	End W23	Feature complete	All planned user stories are available in the test environment.
M6	End W26	Release candidate	System, security, and end-to-end tests pass with no open critical defects.
M7	End W29	Go-live approval	UAT signed off; configurations, deployment and support materials are ready.
M8	W30	Production handover	Smoke tests pass and ownership transfers to operations/support.

Planning Assumptions

- The developer is allocated full time, with approximately 80% of capacity available for planned delivery after ceremonies, support and rework.
- A product owner and representatives from TA, Total Rewards, HROD, HRBP, Division leadership and IT/security are available for weekly clarification and scheduled reviews.
- A supported application platform, identity provider, email service, database, document storage and deployment environment are selected by the end of Week 2.
- MS Forms integration is limited to a supported handoff/import/API pattern; building a new public candidate portal is outside this baseline.
- One offer-letter template and one primary notification channel configuration are included initially; extensive template variants or Teams integration require re-estimation.
- Business users supply approved salary matrices, approver mappings, SLA thresholds, legal entities, test data and offer templates on schedule.
- UAT execution is performed by business users; the developer supports triage, remediation and regression.
- Calendar duration excludes major organizational shutdowns and assumes stakeholder decisions are returned within two business days.

Dependencies and Schedule Risks

Rating	Risk / Dependency	Schedule Effect	Mitigation
High	Late platform/integration decisions	Delays architecture and can cause rework across intake, notifications and deployment.	Confirm technical stack and service owners in Week 1; time-box proof-of-concept work.
High	Unavailable or changing salary/approval rules	Blocks calculation and workflow acceptance.	Obtain approved matrices and decision tables by Week 3; version all rule changes.
High	Single-developer concentration	Illness, production support or competing work directly affects the critical path.	Protect allocation, document weekly, automate tests/deployment, and keep a visible contingency backlog.
Medium	Identity, email, storage or MS Forms access	External approvals and tenant configuration can create idle time.	Raise access requests during discovery and use stubs/mocks until credentials arrive.

Rating	Risk / Dependency	Schedule Effect	Mitigation
Medium	Slow stakeholder review/UAT	Defects and rule gaps surface late.	Run demos at M2-M5 and book UAT participants before Week 23.
Medium	Security/privacy findings	Compensation and candidate documents require strict access and auditability.	Threat-model early; test role boundaries and document access before UAT.

Estimate Boundaries and Change Control

The 30-week baseline is appropriate for planning and sequencing, but it is not a fixed-price commitment. Re-estimate after Week 2 when the platform, integration pattern, security constraints, document templates and reporting expectations are confirmed. Add schedule or trade scope when requirements introduce a public candidate portal, complex legacy migration, multiple offer-letter variants, e-signature, Microsoft Teams integration, advanced analytics, high-availability requirements, or material policy changes.

Recommended Working Cadence

Frequency	Activity
Weekly	Backlog refinement and stakeholder decision session
Every 2 weeks	Demonstration, acceptance review and next-sprint commitment
Continuous	Automated unit/integration checks, audit logging and deployment pipeline
At each milestone	Formal exit review against the gate criteria above
Weeks 27-29	Structured UAT cycles with daily defect triage

Source References

Online Job Offer System - User Stories V2.xlsx

Job Offer Business Logic Rules.docx

Job Offer Programmer Detailed Flowchart - Editable Text.docx

Prepared as a proposed delivery baseline. Dates should be converted from relative weeks to calendar dates after kickoff is approved.
